

BROADAIR

J124 TNT- Redfern

Site QA
Penetrations
Core Hole Penetration
Level 1

Report summary


Name	Status	Last Activity
Level 1	pass	15 Dec 2022 11:40am
FP-L1-R - page 3	pass	15 Dec 2022 11:40am

Site QA - Penetrations - Core Hole Penetration - Level 1 - FP-L1-R

First Activity: 15 Dec 2022 11:39am
Last Activity: 15 Dec 2022 11:40am

Checklist: pass
Passed: 12
Failed: 0
N/A: 3

Core Hole Checklist

Penetration details have been captured			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:39am
		Sebastian Lopez	15 Dec 2022 11:39am
IMG-20220815-WA0000.jpg https://conqausercontent.com/raw/a1374341-6c73-4a13-824b-b464e7b34ef0			

Penetration details have been captured




Sebastian
Lopez 15 Dec 2022
11:39am


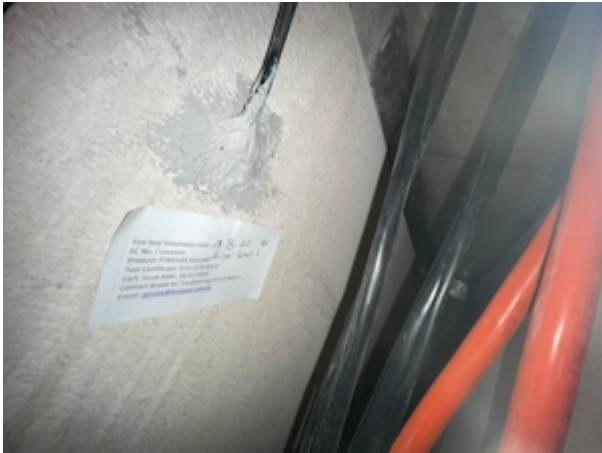
IMG-20220815-WA0002.jpg
<https://conqausercontent.com/raw/3410cc4c-6072-41ac-84c2-6ef2be7909e1>



Sebastian
Lopez 15 Dec 2022
11:39am

IMG-20220815-WA0003.jpg

Penetration details have been captured		
https://conqausercontent.com/raw/59f88ba7-19c5-4da8-911f-30f303fd8951		
	Sebastian Lopez	15 Dec 2022 11:39am
IMG-20220815-WA0005.jpg https://conqausercontent.com/raw/9cc0d421-f19d-4f14-9062-a5ecbaf82e14		

Penetration details have been captured			
<div></div> <div>IMG-20220815-WA0004.jpg https://conqausercontent.com/raw/3e95d5cf-a357-4046-a679-b9c9a59525e6</div>		Sebastian Lopez	15 Dec 2022 11:39am
<div></div> <div>IMG-20220815-WA0001.jpg https://conqausercontent.com/raw/898fb64a-22d4-4965-838f-92f5cea70234</div>		Sebastian Lopez	15 Dec 2022 11:39am
Inside riser		Sebastian Lopez	15 Dec 2022 11:39am
Penetration ID #1:			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:39am

Penetration ID #1:



Sebastian
Lopez

15 Dec 2022
11:40am

20221115_141913.jpg



<https://conqausercontent.com/raw/396cc428-a6e4-46f2-91cc-a4b5544d8e2e>




Sebastian
Lopez

15 Dec 2022
11:40am

20221115_141921.jpg

Penetration ID #1:		
https://conqausercontent.com/raw/ec374506-b6b3-4508-8407-2af94dec1293		
	Sebastian Lopez	15 Dec 2022 11:40am
https://conqausercontent.com/raw/fc93694a-8f84-4168-8b26-7d7f04d95a00		
	Sebastian Lopez	15 Dec 2022 11:40am
https://conqausercontent.com/raw/0a582304-6914-471a-aff3-8a7a9e9c9495		

Penetration ID #1:			
 <p>20221115_141852.jpg https://conqausercontent.com/raw/a3ad3b0e-c609-42f0-b9e0-d0d0a150b86e</p>		Sebastian Lopez	15 Dec 2022 11:40am
Outside riser		Sebastian Lopez	15 Dec 2022 11:40am
Number of Penetrations			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Core hole max 120mm with Boss Fire FireMastic-HPE sealant (FMHPE-3 / FMHPE-6) filled to a depth of 30mm from either side of wall.			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Cables to be tucked between insulation for a minimum of 300mm each side of the penetration			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
The penetration is labelled and photographic evidence is provided			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Maximum services passing the penetration is not exceeding the following			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am

Three insulated copper pipes with up-to 20mm OD completed with 19mm Fire rated insulation, with cable up-to one Power Cable and one Data Cable as per EWFA-49599300.7			
Status	N/A	Sebastian Lopez	15 Dec 2022 11:40am
Or			
Status	N/A	Sebastian Lopez	15 Dec 2022 11:40am
One Copper pipe to maximum size of 40mm OD Completed with 19mm Fire rated Insulation as per CSIRO FCO-2990 - Wall to bi thickened tp 120mm Deep locally to comply with CSIRO FCO-2990			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Notes/Additional Comments:			
Status	N/A	Sebastian Lopez	15 Dec 2022 11:40am

Sign Off

Sign-Off Completed as per below (Pass once complete)			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Contract/Subcontractor Assessor Sign Off			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Builder Representative Sign Off			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Request Sign-Off(s) + Click to Add Signature(s)			
Status	Pass	Sebastian Lopez	15 Dec 2022 11:40am
Inspection Date:			

